


# Highland Laurels To Forest Garden

## Weeks 4, 5, 6, and 7 Major Work Scope

## Report and Update for May 23, 2026

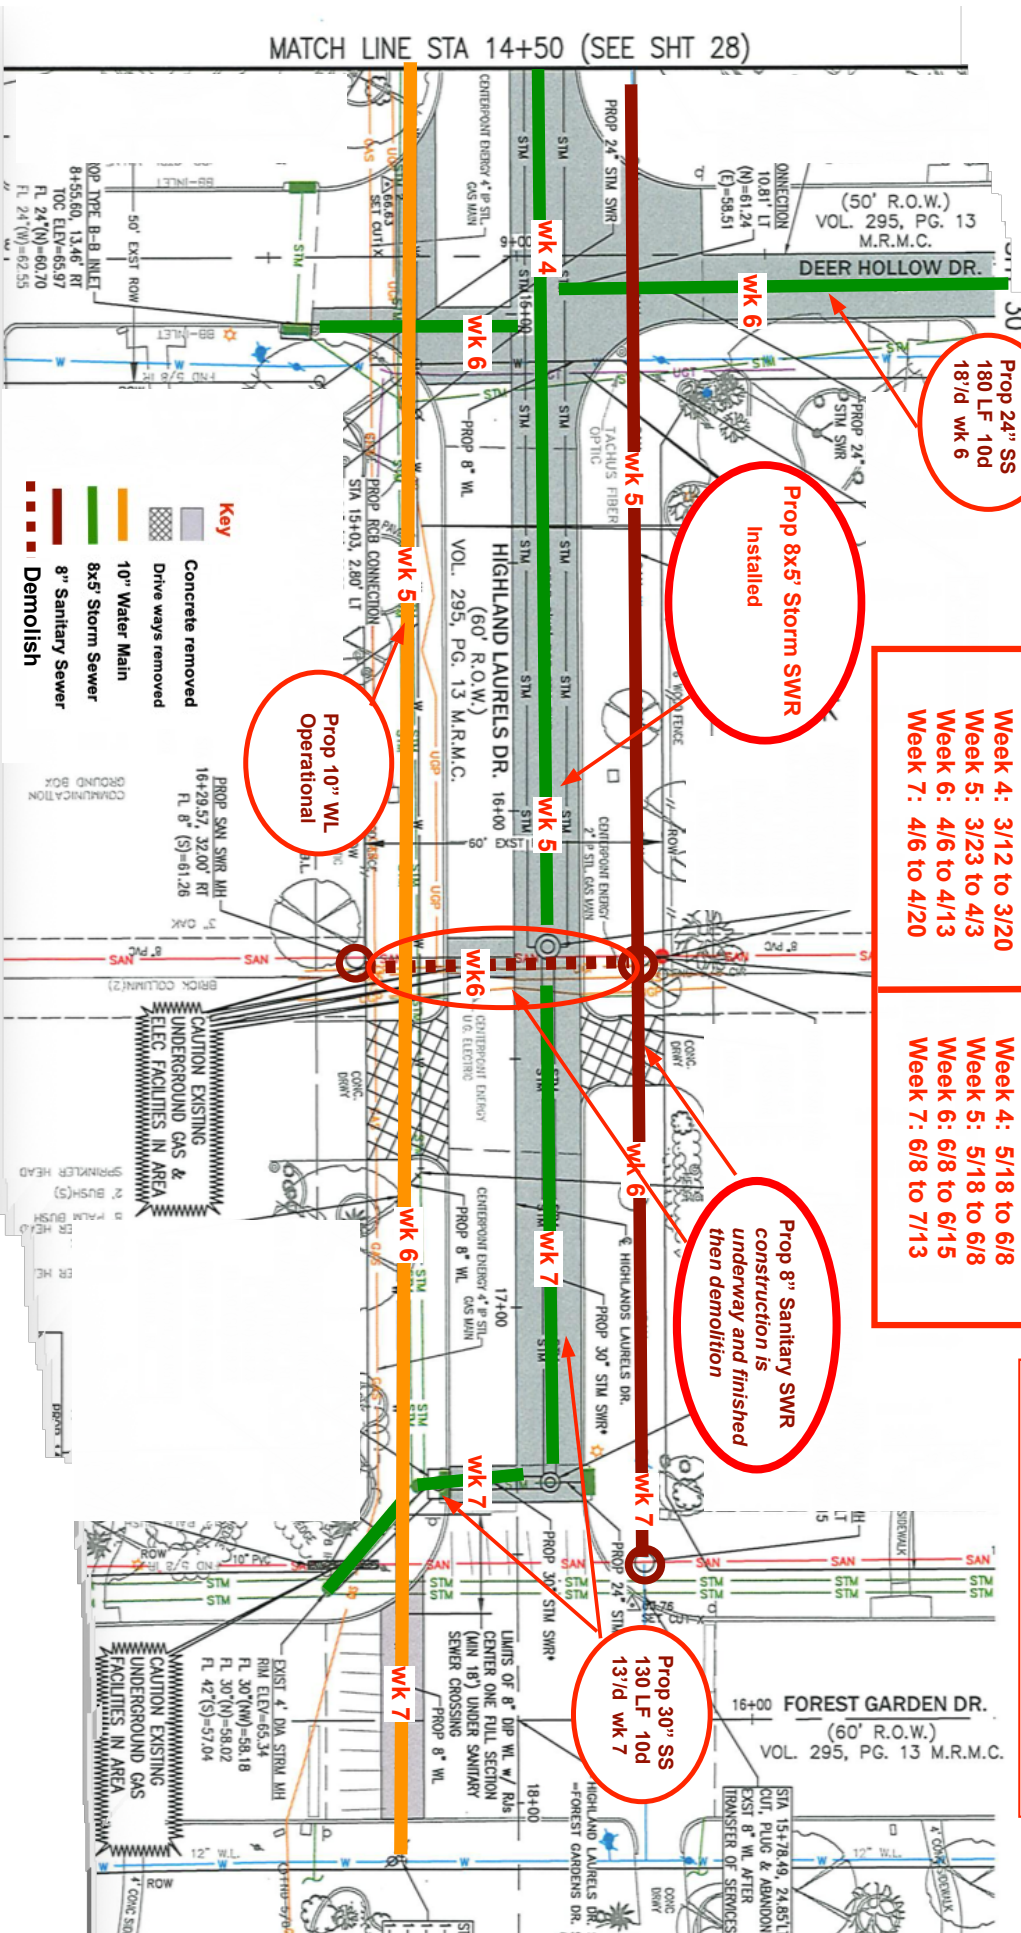

baseline @ 2/01	forecast @ 5/23
Week 4: 3/12 to 3/20	Week 4: 5/18 to 6/8
Week 5: 3/23 to 4/3	Week 5: 5/18 to 6/8
Week 6: 4/6 to 4/13	Week 6: 6/8 to 6/15
Week 7: 4/6 to 4/20	Week 7: 6/8 to 7/13

critical path: 8" sanitary sewer line; 24" DH Storm Sewer labeled as week 6, then the 30" storm sewer line labeled as week 7.

**FIFTH REPLANNING BY THE CONTRACTOR???**  
 The final plan is not clear. Once the 8" Sanitary Sewer is completed, there are many activities for the large excavator and how that will be deployed can take many turns. It could continue down Highland Laurels to Forest Garden with the 30" Storm Sewer and finish the tie into the existing storm sewer (Wk 7). It could then move to Deer Hollow and do the 24" Storm Sewer there. (Wk 6). It could then move to install the last 8x5' box culvert and start the paving headed back to Forest Garden. Or it could be done in the reverse order. Not sure enough time is allowed for paving, curbing and landscaping to finish the project.
